


Town of Groton, Massachusetts

Florence Roche Elementary School

Module 3 | Preferred Schematic Response

May 5, 2020

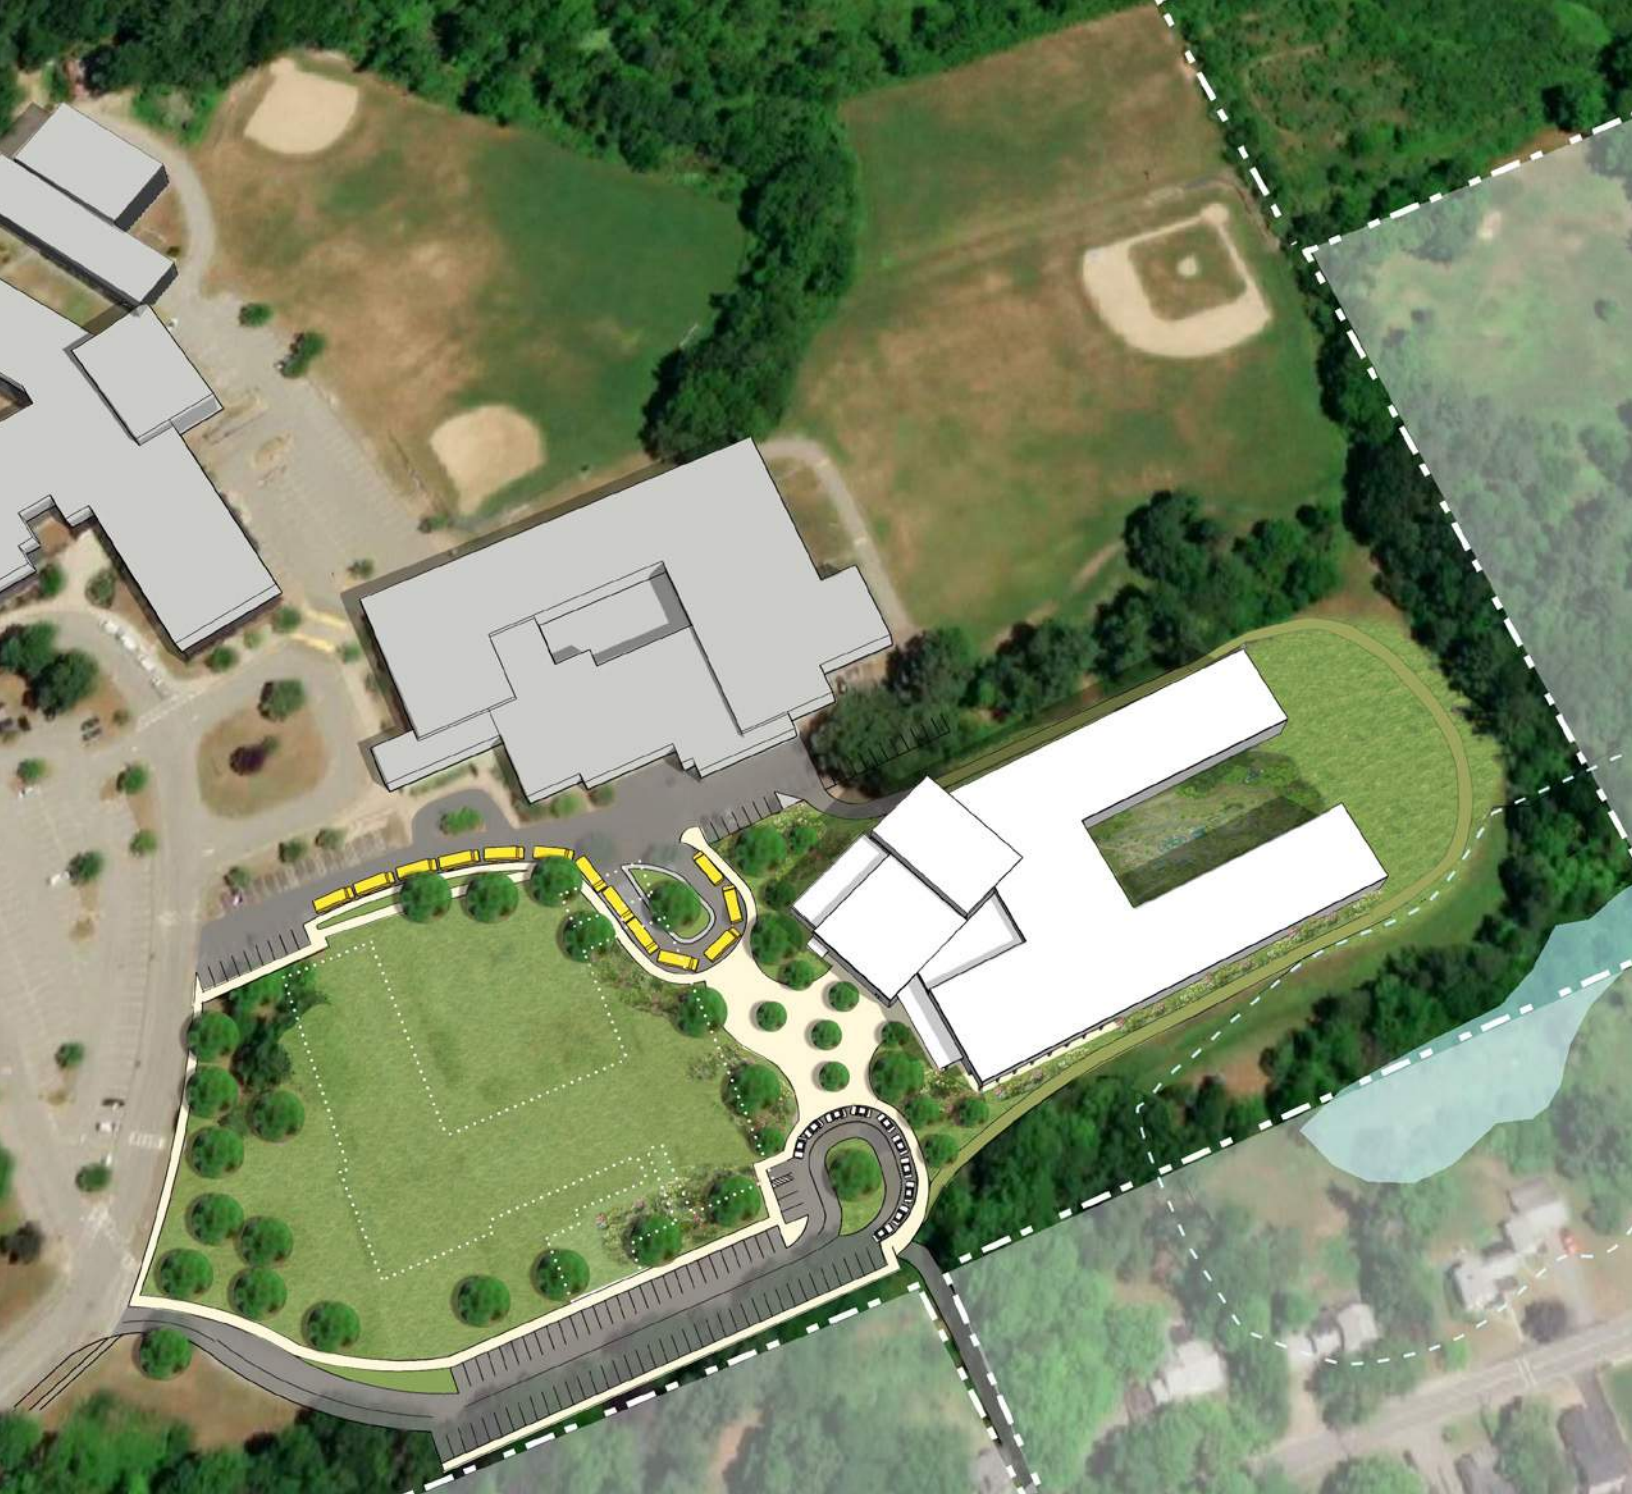

studiog architects
building **sustainable** communities

LEFTFIELD
THE RIGHT CHOICE IN PROJECT MANAGEMENT

MSBA Project #201706730010



TABLE OF CONTENTS

1 INTRODUCTION

1.1	Process Overview	2
1.2	Summary of Updated Project Schedule	29
1.3	Summary of Final Evaluation of Existing Conditions	31
1.4	Summary of the Final Evaluation of Alternatives	32
1.5	Summary of District's Preferred Solution	38
1.6	MSBA PDP Review & Response	39

2 EVALUATION OF EXISTING CONDITIONS

2.1	Narrative of Changes	1
2.2	Updated Evaluation of Existing Conditions	2

3 FINAL EVALUATION OF ALTERNATIVES

	OPTION 2: ADDITION / RENOVATION	4
3.1	Prospective Site Analysis	5
3.2	Evaluation of Construction Impact	6
3.3	Conceptual Drawings	10
3.4	Structural Systems	12
3.5	Utilities	13
3.6	Building Systems	14
3.7	Proposed Budget & Cost Estimate	14
3.8	Permitting Requirements & Approval Schedule	16
3.9	Proposed Design & Construction Schedule	16
3.10	MSBA Summary of Preliminary Design Pricing	17

TABLE OF CONTENTS

3 FINAL EVALUATION OF ALTERNATIVES continued

OPTION 3: NEW CONSTRUCTION: SITE A – Behind Existing Florence Roche	18
3.1 Prospective Site Analysis	20
3.2 Evaluation of Construction Impact	22
3.3 Conceptual Drawings	26
3.4 Structural Systems	28
3.5 Utilities	30
3.6 Building Systems	34
3.7 Proposed Budget & Cost Estimate	72
3.8 Permitting Requirements & Approval Schedule	74
3.9 Proposed Design & Construction Schedule	76
3.10 MSBA Summary of Preliminary Design Pricing	80
OPTION 4: NEW CONSTRUCTION: SITE B – Behind Middle School South	81
3.1 Prospective Site Analysis	82
3.2 Evaluation of Construction Impact	83
3.3 Conceptual Drawings	86
3.4 Structural Systems	88
3.5 Utilities	89
3.6 Building Systems	90
3.7 Proposed Budget & Cost Estimate	90
3.8 Permitting Requirements & Approval Schedule	92
3.9 Proposed Design & Construction Schedule	92
3.10 MSBA Summary of Preliminary Design Pricing	93

TABLE OF CONTENTS

4 PREFERRED SOLUTION

4.1	Educational Program – Clean Version*	3
4.2	Preferred Solution Space Summary	21
4.3	Preliminary LEED-S Scorecard	25
4.4	Conceptual Floor Plans of Preferred Solution	28
4.5	Site Plan of Preferred Solution	30
4.6	Total Project Budget & Local Funding	35
4.7	Updated Project Schedule	38

5 LOCAL ACTIONS & APPROVALS

5.1	Certified SBC Meeting Information & Presentation Materials	1
5.2	Local Actions & Approvals Certification	1
5.3	Approval & Public Notification of School Configuration Changes	1

6 APPENDIX

1.1	School Tours	1
1.1	Student Worksheet Samples	13
1.1	Sustainability Workshop	55
1.6	MSBA PDP Review & Response	89
3.1	Site Analysis	115
3.6	MEP / FP Report	123
3.7	Cost Estimate	157
3.8	Town of Groton Guide to Permitting	199
3.8	Land Use Department Form of Intent	213
3.8	Massachusetts Historic Commission Response	217
4.1	Educational Program – Red-Lined Version	219
4.6	Construction Estimate	253
4.6	Project Estimate	275
4.6	Municipal Projects	277
4.6	Capital Budget Statement	287
5.1	Certified SBC Meeting Information & Presentation Materials	295

* Refer to Appendix 6/4.1 – Educational Program - Red-Lined Version

ACKNOWLEDGMENTS

Thank you to these individuals and organizations for their contributions to this Feasibility Study:

MASSACHUSETTS SCHOOL BUILDING AUTHORITY

Christina Forde – Project Manager
Brian Lynch – Project Coordinator

FLORENCE ROCHE BUILDING COMMITTEE

Sherry Kersey – Director of Business & Finance
Dr. Laura Chesson – Superintendent of Schools
Mark Haddad – Town Manager of Groton
Marlena Gilbert – School Committee Chair
Fay Raynor – Chairperson of School Building Committee
Ryan McLane – School Committee Member
Brian O'Donoghue – Principal, Florence Roche Elementary School
Jake Lewon – Dunstable Advisory Committee
Colby Doody – Groton Finance Committee
Alison Manugian – Groton Select Board
Luke Callahan – Director of Technology
Berta Erickson – Senior & Active Community Member

GROTON SELECT BOARD

Alison Manugian – Chair
Joshua Degen – Vice-Chair
John Reilly – Clerk
Rebecca 'Becky' Pine – Member
John Giger – Member

GROTON-DUNSTABLE SCHOOL COMMITTEE

Marlena Gilbert – Chair
Ryan McLane – Vice-Chair
Brian LeBlanc – Member
Jeff Kubick – Member
Fay Raynor – Member
Whitney Healey – Member
Peter Cronin – Member

OWNER'S PROJECT MANAGER

LEFTFIELD, LLC

DESIGN TEAM

Studio G Architects (SGA) – Designer
New Vista Design – Educational Planning
Samiotes – Environmental Permitting & Civil Engineer
Terraink – Landscape Architects
Engineer's Design Group (EDG) – Structural Engineer
RW Sullivan – MEP / FP Engineer
Vantage Technology Group – Security Consultant
EFI Global – Hazardous Materials Consultant
LAHLAF Geotechnical Consulting – Geotechnical Engineer
CDW Consultants – Geoenvironmental Engineer
PM&C – Cost Estimating
Building, Fire & Access – Code Consultant
